


Construction Update
Middlebury Bridge & Rail Project

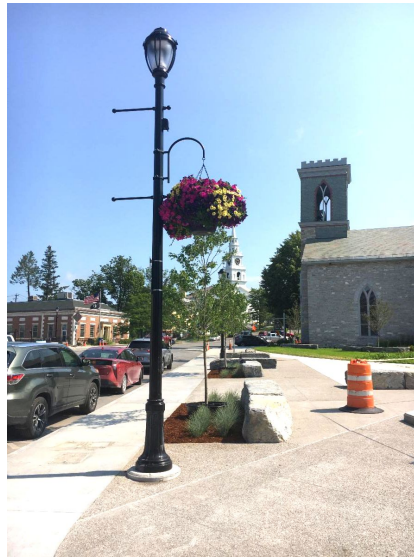

The above photo shows fresh plantings in front of St. Stephen's Church. Summer is in full bloom in downtown Middlebury!

DATE: July 16, 2021

TRAFFIC IMPACT

Construction vehicles will be entering and exiting Printer's Alley from Main Street and the Marble Works from Seymour Street. Pedestrians, bicyclists, and drivers should proceed with caution. This applies to the Fifield Farm marshaling yard on Route 30 south of town as well.

CONSTRUCTION ACTIVITIES

Crews will pour the remaining sections of concrete for the south cap wall next week. Kubricky will backfill the U-walls parallel to the upper Battel drive and Landshapes will restore plantings and ashlar blocks along the driveway. Battel drive is anticipated to reopen in late July.

Waters began installing a concrete curb that will run from the bottom of Printer's Alley north along the rail corridor. A&K Slip Forming will finish pouring concrete for the Amtrak rail platform on Friday.

In Lazarus Park, Lafayette will continue installing the decorative railing along the north cap wall. It is anticipated that Waters will complete the stairs that lead from Main Street to the Marble Works. Landshapes will begin work on the labyrinth. They will landscape Lazarus Park and the area between the Post Office and the rail corridor.

OTHER UPDATES

The related Middlebury Paving Project is now in Phase 2. The contractor is milling Route 125 (College Street), Route 30 (S. Main Street), Cross Street, and Main Street near Merchant's Row (downtown), as well as Court Square to tie in with completed Phase 1. Please drive with caution, especially motorcyclists.

LOCATION: Triangle Park, Printer's Alley, and Lazarus Park

PROJECTED COMPLETION: August 2021

CONTACT

Shawna Kitzman, Public Information Consultant
802-230-7648
skitzman@fhstudio.com

Project Fact Sheet



To learn more about VTrans Construction Projects, visit our [projects website](#).
