Project : 12A026(91)

BRATTLEBORO IM 091-1(65)

Date: 11 Mar 2016

Time: 16:26:31

Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	VTRANS WBS	VTRANS OBS
010.005	Scoping Funded	22	22	010	PROJECT DEVELOPMENT
020.06	Local Concerns Letter	33	33	020	PROJECT DEVELOPMENT
030.01.01	Survey	44	44	030.01	SURVEY
030.01.02	Traffic Data	22	22	030.01	TECHNICAL SUPPORT
030.01.03	Hydraulics - Preliminary	33	33	030.01	HYDRAULICS
030.01.04	Utilities - Existing	33	33	030.01	UTILITIES
030.01.05	ROW - Existing	33	33	030.01	RIGHT-OF-WAY
030.01.06	Resource Identification	88	88	030.01	ENVIRONMENTAL
030.01.07	Geotechnical Assessment	33	33	030.01	MATERIALS & RESEARCH
030.01.09	Railroad Crossing Criteria	66	66	030.01	PROJECT DEVELOPMENT
030.04.01	Develop Alternatives	44	44	030.04	PROJECT DEVELOPMENT
030.04.011	Develop Risk Registry	44	44	030.04	PROJECT DEVELOPMENT
030.04.012	Develop Traffic Management Plan	44	44	030.04	PROJECT DEVELOPMENT
030.04.013	Project Collaboration - Scope Review Period	44	44	030.04	PROJECT DEVELOPMENT
030.04.015	Management Approval of Scope	22	22	030.04	PROJECT DEVELOPMENT
030.04.02	Alternatives Presentation/Refinement	44	44	030.04	PROJECT DEVELOPMENT
030.04.03	Alternative Accepted	0	0	030.04	PROJECT DEVELOPMENT
030.04.04	Transfer to Design	22	22	030.04	PROJECT DEVELOPMENT
040.04	NEPA Document	88	88	040	ENVIRONMENTAL
050.01	Develop Conceptual Plans	44	44	050	PROJECT DEVELOPMENT
050.02	Public Meeting/Hearing/Refinement	44	44	050	PROJECT DEVELOPMENT
050.03	Project Defined	0	0	050	PROJECT DEVELOPMENT
060.01.01	Develop Base Technical Concept - Design Build	132	132	060	PROJECT DEVELOPMENT
060.01.02	Develop RFQ - Design Build	44	44	060	PROJECT DEVELOPMENT
060.012.01	BTC QAU Review Period - Design Build	22	22	060	PROJECT DEVELOPMENT
060.012.02	RFQ Review Period - Design Build	22	22	060	PROJECT DEVELOPMENT
060.014.01	BTC Constructability Review- Design Build	11	11	060	PROJECT DEVELOPMENT
060.03	Geotechnical Analysis	110	110	060	MATERIALS & RESEARCH
060.05.01	Environmental Coordination - Design Build	110	110	060	ENVIRONMENTAL
060.06	Utility Relocation Routing	88	88	060	UTILITIES
060.07	Property Owner Contact	44	44	060	PROJECT DEVELOPMENT
060.08.01	Address BTC Review Comments - Design Build	22	22	060	PROJECT DEVELOPMENT
060.08.02	Address RFQ Review Comments - Design Build	22	22	060	PROJECT DEVELOPMENT
060.08.03	Advertise RFQ - Design Build	27	27	060	FINANCE & ADMINISTRATION
060.08.04	Evaluate RFQ - Design Build	33	33	060	PROJECT DEVELOPMENT
060.08.045	Secretary Approval of Shortlist - Design Build	5	5	060	FINANCE & ADMINISTRATION
060.08.05	Post RFQ Shortlist - Design Build	5	5	060	FINANCE & ADMINISTRATION
060.085	Preliminary ROW Estimate/ROW STIP Verification	44	44	060	PROJECT DEVELOPMENT
060.09	ROW Acquisition Authorization	66	66	060	RIGHT-OF-WAY
060.10	NEPA Re-evaluation	22	22	060	ENVIRONMENTAL
060.11	Utility Agreements	44	44	060	UTILITIES

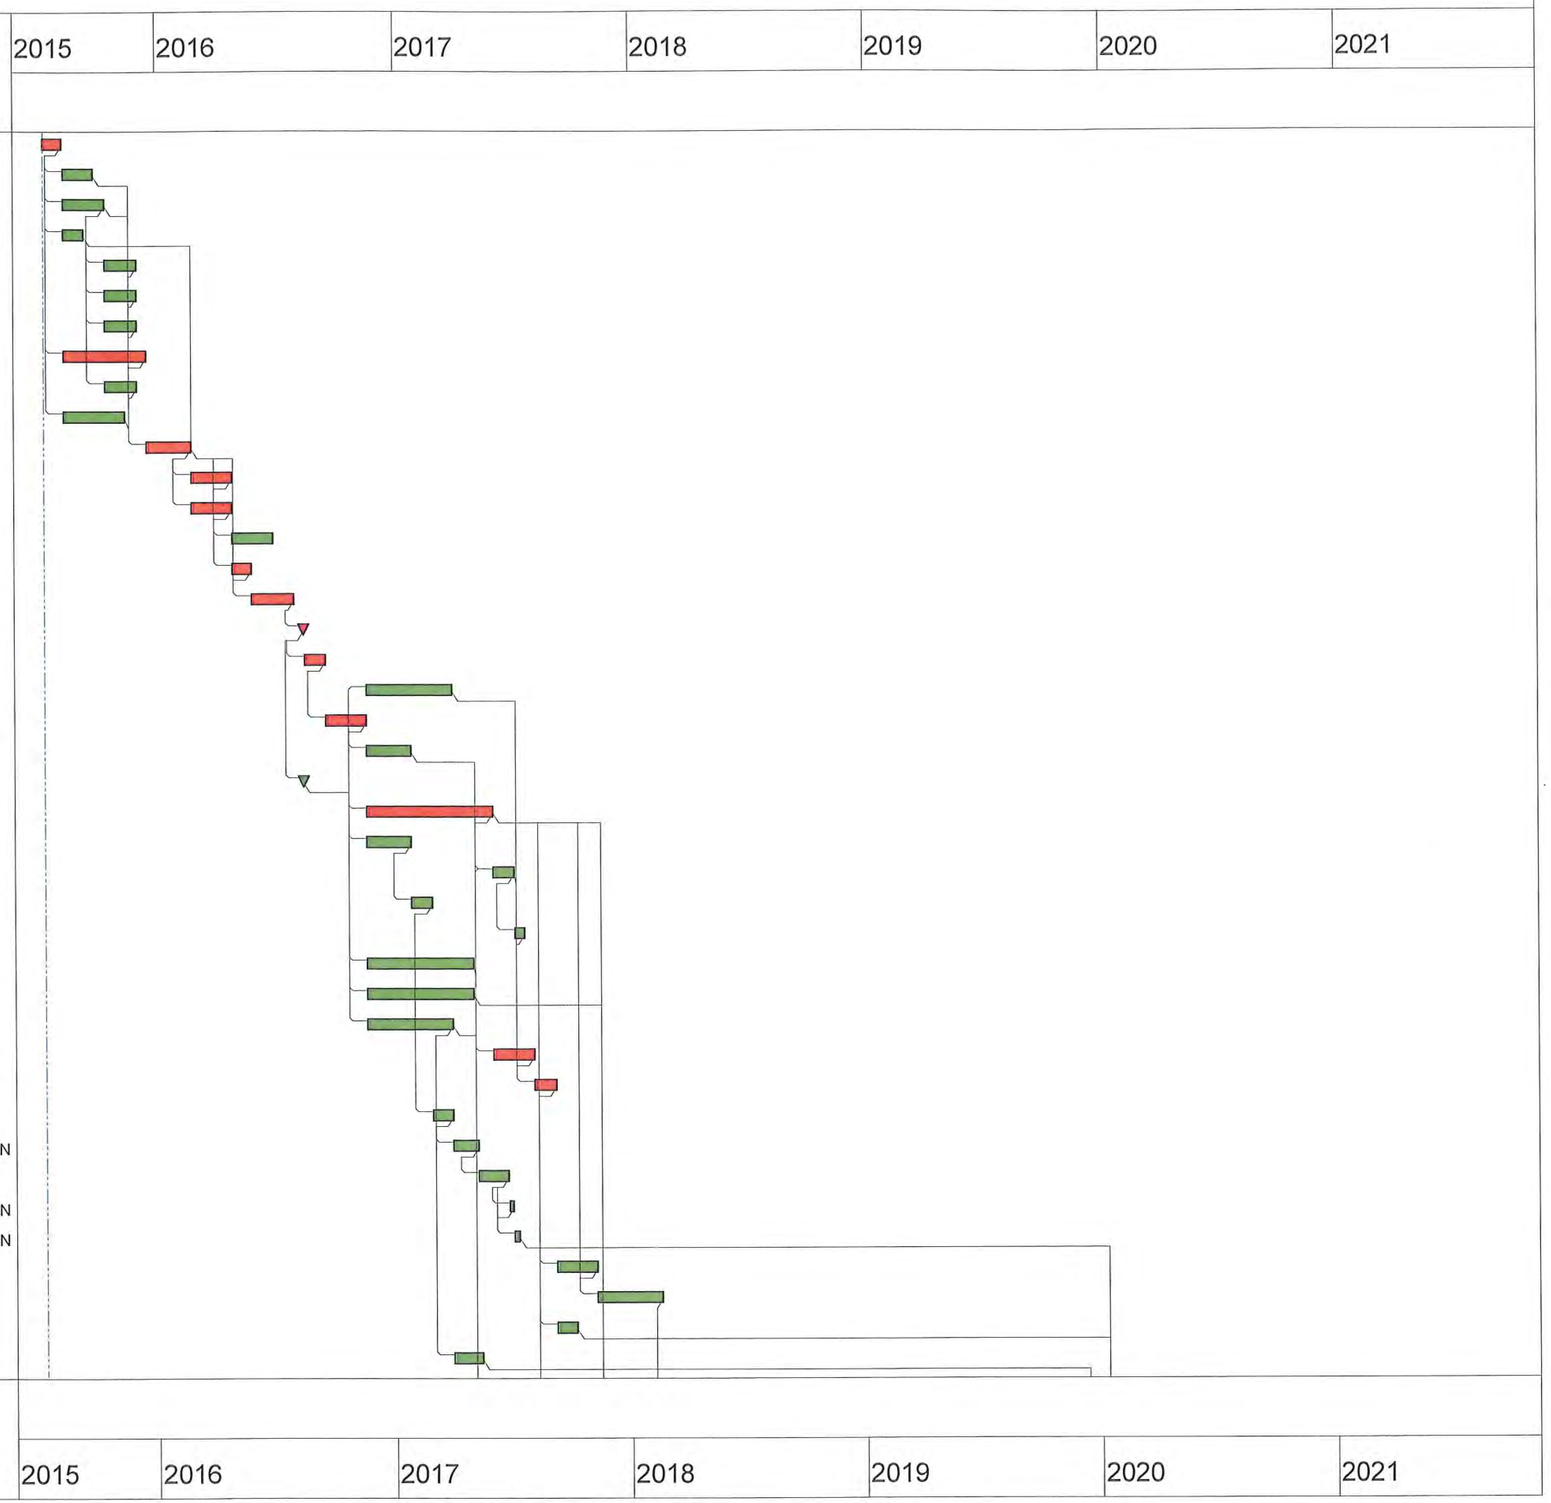

ProjectView

Project : 12A026(91)

BRATTLEBORO IM 091-1(65)

Date: 11 Mar 2016

Time: 16:26:31

Activity Name	Activity Description	Rem. Dur.	Orig. Dur.	VTRANS WBS	VTRANS OBS
060.15	Railroad Aggreements & Special Provisions	88	88	060	PROJECT DEVELOPMENT
080.01	Develop ROW Plans and Titles	88	88	080	RIGHT-OF-WAY
080.02	Legal Document Preparation	33	33	080	RIGHT-OF-WAY
080.03	Final ROW Plans and Documents Complete	0	0	080	RIGHT-OF-WAY
090.02	Appraisal	132	132	090	RIGHT-OF-WAY
090.022	Waiver Valuation Estimates	22	22	090	RIGHT-OF-WAY
090.024	Appraisal Review	22	22	090	RIGHT-OF-WAY
090.03	Negotiation	88	88	090	RIGHT-OF-WAY
090.0351	Necessity Complaint to Court	0	0	090	RIGHT-OF-WAY
090.0352	Contesting of Necessity	22	22	090	RIGHT-OF-WAY
090.0353	Court to Schedule Necessity Hearing	90	90	090	RIGHT-OF-WAY
090.0354	Necessity Hearing	0	0	090	RIGHT-OF-WAY
090.0355	Necessity/Condemnation Order	30	30	090	RIGHT-OF-WAY
090.0356	Necessity Appeal Period	30	30	090	RIGHT-OF-WAY
090.0357	Compensation Appeal Period	30	30	090	RIGHT-OF-WAY
090.037	Minor Alterations Condemnation	66	66	090	RIGHT-OF-WAY
090.04	Compensation	15	15	090	RIGHT-OF-WAY
090.05	ROW Clear	0	0	090	RIGHT-OF-WAY
100.01.01	Develop RFP - Design Build	132	132	100	PROJECT DEVELOPMENT
100.015.01	Develp RFP Project Special Provisions - Design Build	22	22	100	PROJECT DEVELOPMENT
100.02.01	RFPQAU Review Period - Design Build	22	22	100	PROJECT DEVELOPMENT
100.03	Utility Clearance & Special Provisions	22	22	100	UTILITIES
100.06.01	Address RFP Review Comments - Design Build	22	22	100	PROJECT DEVELOPMENT
100.06.02	DB short-list review of RFP-Design Build	16	16	100	PROJECT DEVELOPMENT
100.06.03	Address short-list review comments-Design Build	11	11	100	PROJECT DEVELOPMENT
100.11	Submit Contract Plans	0	0	100	PROJECT DEVELOPMENT
110.01	Proposal Preparation	16	16	110	FINANCE & ADMINISTRATION
110.02.01	Advertise RFP - Design Build	0	0	110	FINANCE & ADMINISTRATION
110.02.02	Pre-Proposal Meeting - Design Build	11	11	110	PROJECT DEVELOPMENT
110.02.03	Alternative Technical Concept Process - Design Build	85	85	110	PROJECT DEVELOPMENT
110.02.04	RFP Questions - Design Build	85	85	110	FINANCE & ADMINISTRATION
110.02.05	Technical Proposal Development - Design Build	99	99	110	PROJECT DEVELOPMENT
110.02.06	Evaluate Technical Proposals - Design Build	44	44	110	PROJECT DEVELOPMENT
110.02.07	Secretary Approval of RFP Scoring - Design Build	5	5	110	FINANCE & ADMINISTRATION
110.02.08	Open Price Proposals - Design Build	0	0	110	FINANCE & ADMINISTRATION
110.02.09	Proposal Clarificarions	22	22	110	PROJECT DEVELOPMENT
110.03	Contract Award	22	22	110	FINANCE & ADMINISTRATION
120.10	Pre-Construction	88	88	120	PROJECT DEVELOPMENT
120.11	Active Construction	176	176	120	PROJECT DEVELOPMENT

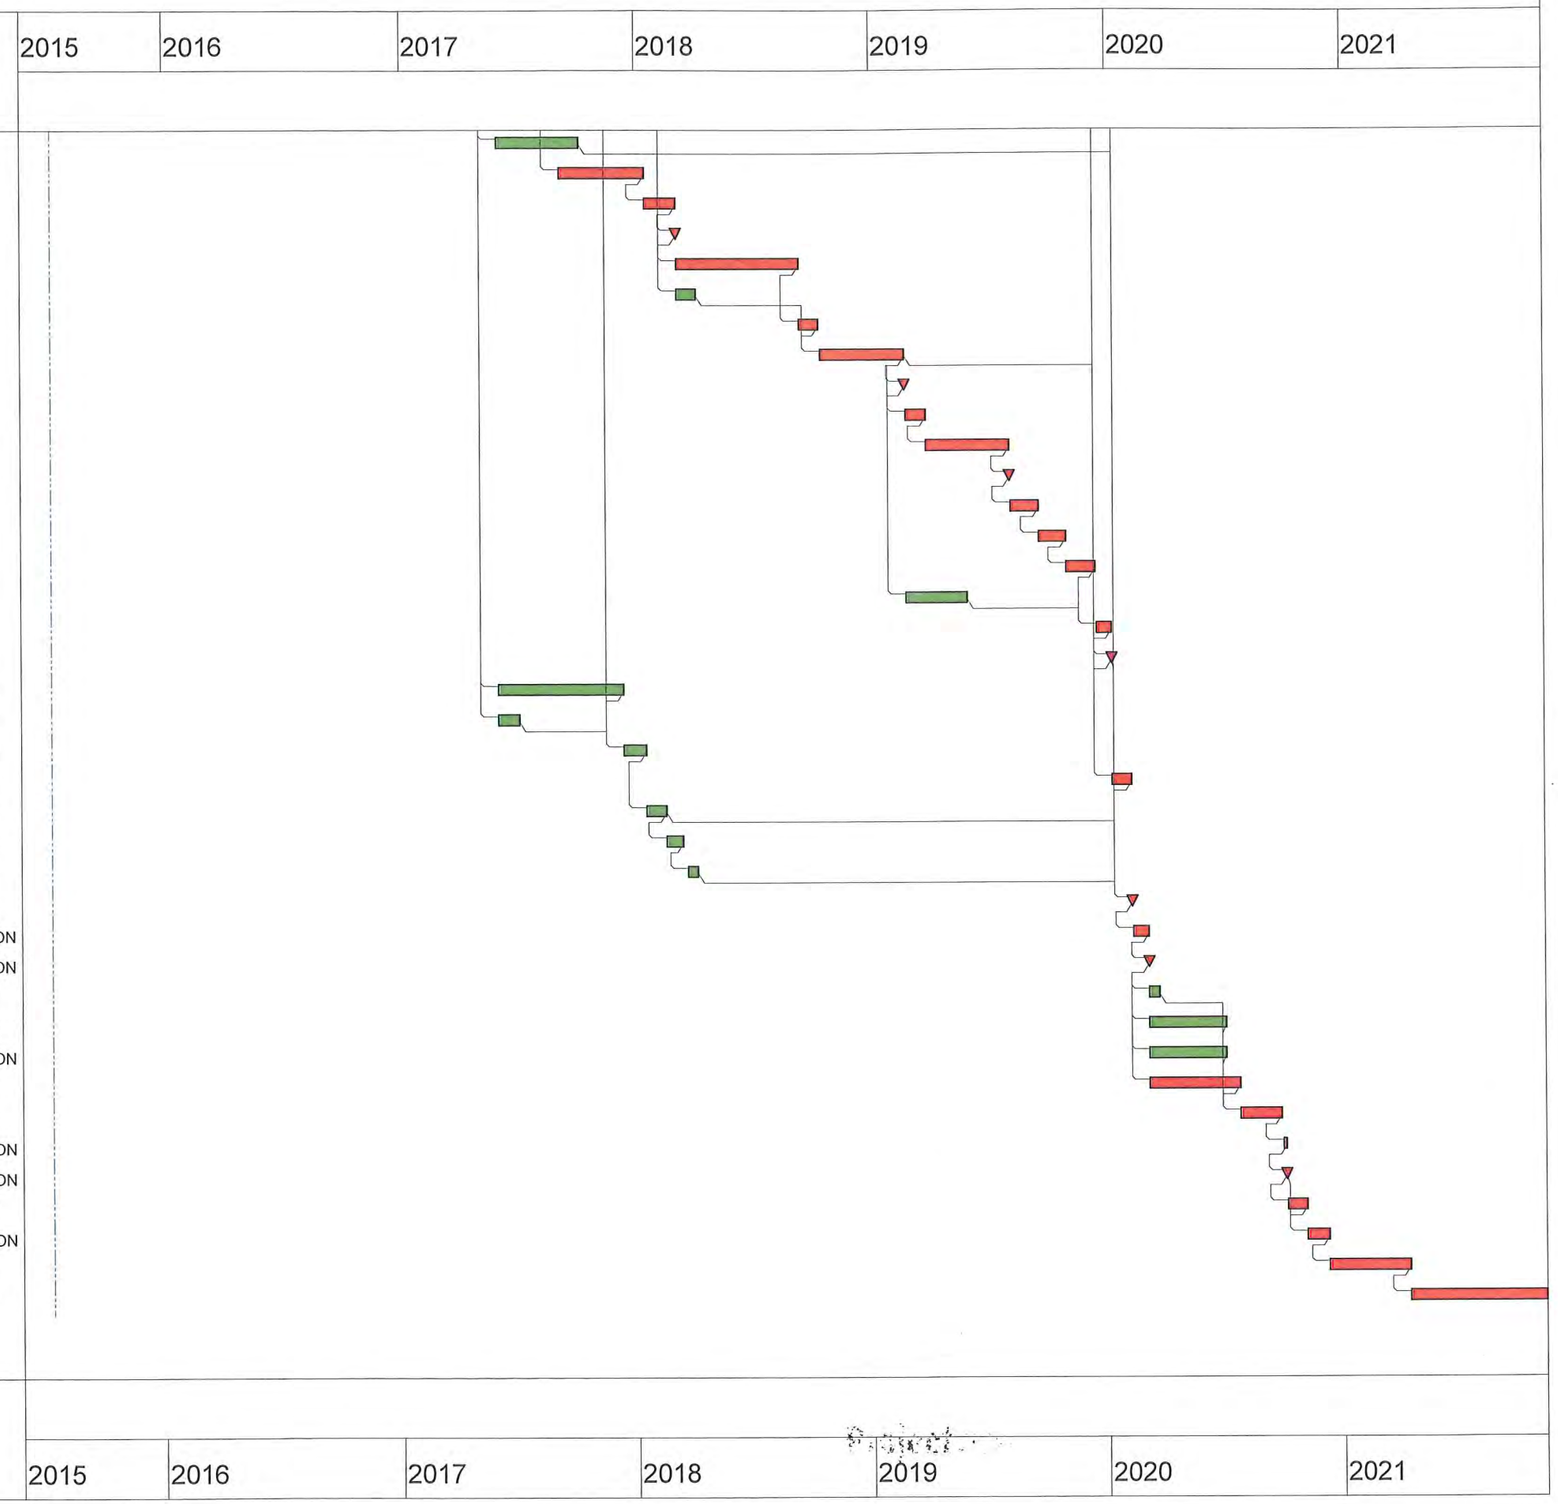

ProjectView
